


Project Management for Engineering and Construction

Second Edition



Garold D. Oberlender

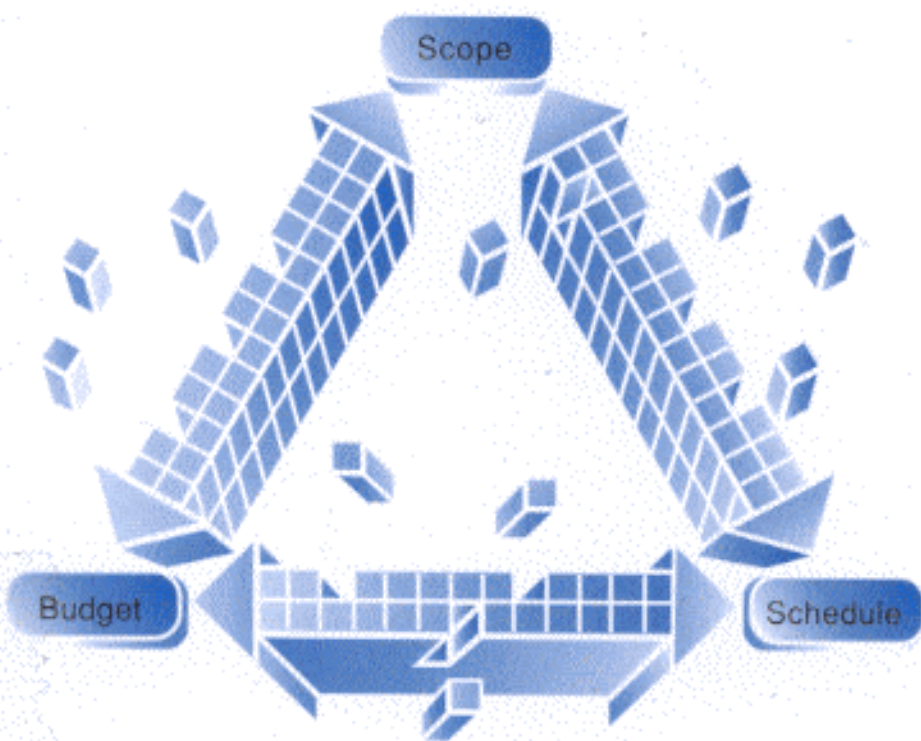

McGRAW-HILL INTERNATIONAL EDITIONS
Civil Engineering Series

CONTENTS

1	INTRODUCTION	1
	Purpose of this Book	1
	Arrangement of this Book	2
	Definition of a Project	4
	Responsibilities of Parties	6
	Who Does the Project Manager Work For?	7
	Purpose of Project Management	8
	Types of Management	9
	Functions of Management	10
	Key Concepts of Project Management	11
	Role of the Project Manager	12
	Professional and Technical Organizations	14
	Questions for Chapter 1—Introduction	15
	References	16
2	WORKING WITH PROJECT TEAMS	17
	Project Teams	17
	Teamwork	18
	Teams for Small Projects	18
	Working with Multiple Teams	19
	Design Teams	20
	Construction Teams	21
	Team Management	22
	Teams and the Project Manager's Responsibilities	22
	Key Factors in Team Leadership	23
	Team Building	24
	Motivating Teams	25
	Conflict Management	27

Developing a Consensus	28
Team Conduct	28
Questions for Chapter 2—Working with Project Teams	29
References	30
3 PROJECT INITIATION	31
Design and Construction Process	31
Advances in the Engineering and Construction Process	33
Private versus Public Projects	33
Contractual Arrangements	33
Phases of a Project	36
Owner's Study	38
Owner's Needs and Project Objectives	38
Project Scope Definition	40
Project Strategy	42
Selection of Design Firms and Construction Contractors	42
Partnering	44
Questions for Chapter 3—Project Initiation	45
References	45
4 EARLY ESTIMATES	47
Importance of Early Estimates	47
Classification of Early Estimates	47
Estimating Work Process	49
Importance of Team Alignment in Preparing Early Estimates	51
Scope Definition and Early Estimates	52
Preparing Early Estimates	55
Organizing to Prepare Estimates	55
Establishing an Estimate Work Plan	56
Methods and Techniques	58
Cost-Capacity Curves	58
Capacity Ratios Raised to an Exponent	59
Plant Cost per Unit of Production	60
Equipment Factored Estimates	61
Computer-Generated Estimates	62
Estimate Check Lists	63
Estimate Documentation	63
Estimate Reviews	65
Risk Assessment	66
Risk Analysis	67
Contingency	68
Traditional Methods of Assigning Contingency	68
Percentage of Base Estimate	68
Expected Net Risk	69

Simulation	70
Assessing Estimate Sensitivity	71
Assigning Contingency Based on the Quality and Completeness of the Estimate	72
Estimate Feed-Back for Continuous Improvement	74
Questions for Chapter 4—Early Estimates	76
References	77
5 PROJECT BUDGETING	78
Project Budgets	78
Development of Project Estimates for Budgeting	78
Levels of Accuracy	80
Owner's Estimate for Budgeting	81
Economic Feasibility Study	85
Single Payments	85
Uniform Payment Series	86
Fundamental Equations of Time Value of Money	87
Design Budgets	90
Contractor's Bid	93
Questions for Chapter 5—Project Budgeting	97
References	98
6 DEVELOPMENT OF WORK PLAN	99
Project Manager's Initial Review	99
Owner's Orientation	100
Organizational Structures	101
Work Breakdown Structure	106
Forming the Project Team	108
Kick-Off Meeting	109
Work Packages	110
Follow-Up Work	111
Project Work Plan	113
Questions for Chapter 6—Development of Work Plan	116
References	117
7 DESIGN PROPOSALS	118
Evolution of Projects	118
Project Execution Plan	119
Project Definition	119
Problems in Developing Project Definition	121
Design Proposals	121
Engineering Organization	124
Scope Baseline for Budget	124

Mini-Drawings	130
Development of the Design Work Plan	132
Engineering Project Controls	134
Progress Measurement of Engineering Design	134
Questions for Chapter 7—Design Proposals	138
References	138
8 PROJECT SCHEDULING	139
Project Planning and Project Scheduling	139
Desired Results of Planning	140
Principles of Planning and Scheduling	141
Responsibilities of Parties	142
Planning for Multiple Projects	142
Techniques for Planning and Scheduling	143
Network Analysis Systems	144
Development of CPM Diagram from the WBS	147
Assigning Realistic Durations	150
Computer Applications	152
Schedule Coding System	153
Cost Distribution	157
Resource Allocations for Design	163
Resource Allocations for Construction	164
Program Evaluation and Review Technique (PERT)	164
Successor/Predecessor Relationships	172
Problems Using Successor/Predecessor Relationships	173
Questions for Chapter 8—Project Scheduling	181
References	183
9 TRACKING WORK	185
Control Systems	185
Linking the WBS and CPM	186
Coding Systems for Project Reports	188
Control Schedules for Time and Cost	193
Relationships Between Time and Work	200
Integrated Cost/Schedule/Work	205
Percent Complete Matrix Method	206
Progress Measurement of Design	211
Measurement of Construction Work	213
Project Measurement and Control	216
Earned-Value System	217
Monitoring Project Performance	225
Interpretation of Performance Indices	227
Analysis Tree of Total Float (TF) and Schedule Performance Index (SPI)	227

Causes of Cost/Schedule Variances	228
Trend Analysis and Forecasting	229
Work Status System	233
Questions for Chapter 9—Tracking Work	236
References	239
10 DESIGN COORDINATION	240
Design Work Plan	240
Producing Contract Documents	241
Managing Scope Growth During Design	241
Managing Small Projects	242
Project Team Meetings	243
Weekly/Monthly Reports	244
Drawing and Equipment Index	244
Distribution of Documents	246
Authority/Responsibility Check List	247
Check List of Duties for Design	248
Team Management	248
Evaluation of Design Effectiveness	251
Constructability	253
Post Design Review	255
Questions for Chapter 10—Design Coordination	256
References	256
11 CONSTRUCTION PHASE	258
Importance of Construction	258
Assumptions for Construction Phase	259
Contract Pricing Formats	260
Design/Bid/Build Method of Project Delivery	261
Design/Build Method of Project Delivery	262
Construction Management Method of Project Delivery	262
Bridging Project Delivery Method	263
Fast-Track Projects	264
Turn-Key Projects	264
Design Development and Performance Specifications	264
Key Decisions for Project Delivery	264
Number of Contracts	265
Selection Criteria	265
Contractual Relationship	265
Terms of Payment	265
Prospective Bidders and Bidding	266
Qualification-Based Selection (QBS)	267
Check List for Bidding	269
Keys to a Successful Project	270

Construction Schedules	271
Problems with Construction Schedules	273
Precautions for Construction Submittals	274
Delivery Dates of Owner-Furnished Equipment or Materials	275
Scheduling Contractor Procured and Installed Equipment	275
Contract Schedule Constraints	276
Sequestering Float	276
Schedule Updates	277
Relations with Contractors	277
Check List of Duties	278
Quality Control	278
Dispute Resolutions	281
Job-Site Safety	282
Management of Changes	283
Resource Management	284
Questions for Chapter 11—Construction Phase	286
References	286
12 PROJECT CLOSE OUT	288
System Testing and Start-Up	288
Final Inspection	289
Guarantee and Warranties	290
Lien Releases	290
Record and As-Built Drawings	290
Check List of Duties	291
Disposition of Project Files	291
Post Project Critique	292
Owner Feed-Back	292
Questions for Chapter 12—Project Close Out	292
References	293
13 PERSONAL MANAGEMENT SKILLS	294
Challenges and Opportunities	294
Using New Innovations	294
Human Aspects	297
Assignment of Work	299
Motivation	300
Decision Making	301
Time Management	302
Communications	303
Presentations	305
Meetings	307
Reports and Letters	307

Questions for Chapter 13—Personal Management Skills	309
References	309
14 TOTAL QUALITY MANAGEMENT	311
Background	311
Customer Satisfaction	314
Continual Improvement	315
Management Commitment	318
Training	319
Teamwork	320
Statistical Methods	322
Cost of Quality	324
Supplier Involvement	325
Customer Service	326
Implementation	326
References	328
Appendix A Example Project	329
Appendix B List of EJCDC Contract Documents	348
Appendix C List of AIA Contract Documents	351
Appendix D List of AGC Contract Documents	354
Appendix E MasterFormat™—Master List of Section Titles and Numbers	357

